

# Status of Atoka Projects



March 13, 2025



# Atoka Lake Road



Network: Feb 25, 2025 at 10:55:20 AM CST  
Local: Feb 25, 2025 at 10:55:20 AM CST  
N 34° 25' 46", W 96° 5' 27"  
91° E  
Atoka, OK 74525  
Remark: Lake Atoka Project

Contractor:  
Ellsworth Construction  
Total \$7.56M  
Completion March/April 2025



Network: Feb 14, 2025 at 10:12:26 AM CST  
Local: Feb 14, 2025 at 10:12:27 AM CST  
N 34° 26' 44", W 96° 4' 52"  
186° S  
Atoka, OK 74525  
Remark: Lake Atoka Project



# Pipeline Projects





# Status of Pipeline Projects

Total Length = 98.6 Miles

Pipeline Under Construction = 66.3 Miles

2 Pump Stations Under Construction





# WC-0660 Pump Station O

- Contractor: Wynn Construction Co., Inc.
- Preconstruction Meeting 11/10/2024
- Began Sitework 01/15/2025
- Expected Completion
  - 12/2027





# WC-0871: Pump Station O to Coalgate

Approx. 13.9 Miles

Contractor

- Oscar Renda Contracting, Inc.

Cathodic Protection Commissioning & Training

Hydro-Testing Continues

Expected Completion

- 10/11/2025





# WC-0872: Coalgate to Stonewall





# WC-0873: Stonewall to Ada

- Approx. 9.6 Miles
- Contractor: McKee Utility Contractors, Inc.
- Pipe 100% Installed
- Expected Completion
  - 04/25/2025

Ada Pump Station



Stonewall Pump Station



Google Earth





# WC-0874: Ada to Canadian River

- Approx. 8.8 Miles
- Contractor: McKee Utility Contractors, Inc.
- Pipe is 100% Installed
- Final Walk-Through 02/24/2025





# WC-0876: Canadian River to Konawa

Konawa  
Pump Station

- Approx. 10.5 Miles
- Contractor: McKee Utility Contractors, Inc.
- Began Clear & Grub
- Expected Completion
  - 07/2027

Canadian River


Image © 2024 Airbus

Google Earth



# WC-1011: Konawa Pump Station

- Contractor: Archer Western
- Pre-Construction Meeting 01/29/2025
- Expected Completion
  - March 2028

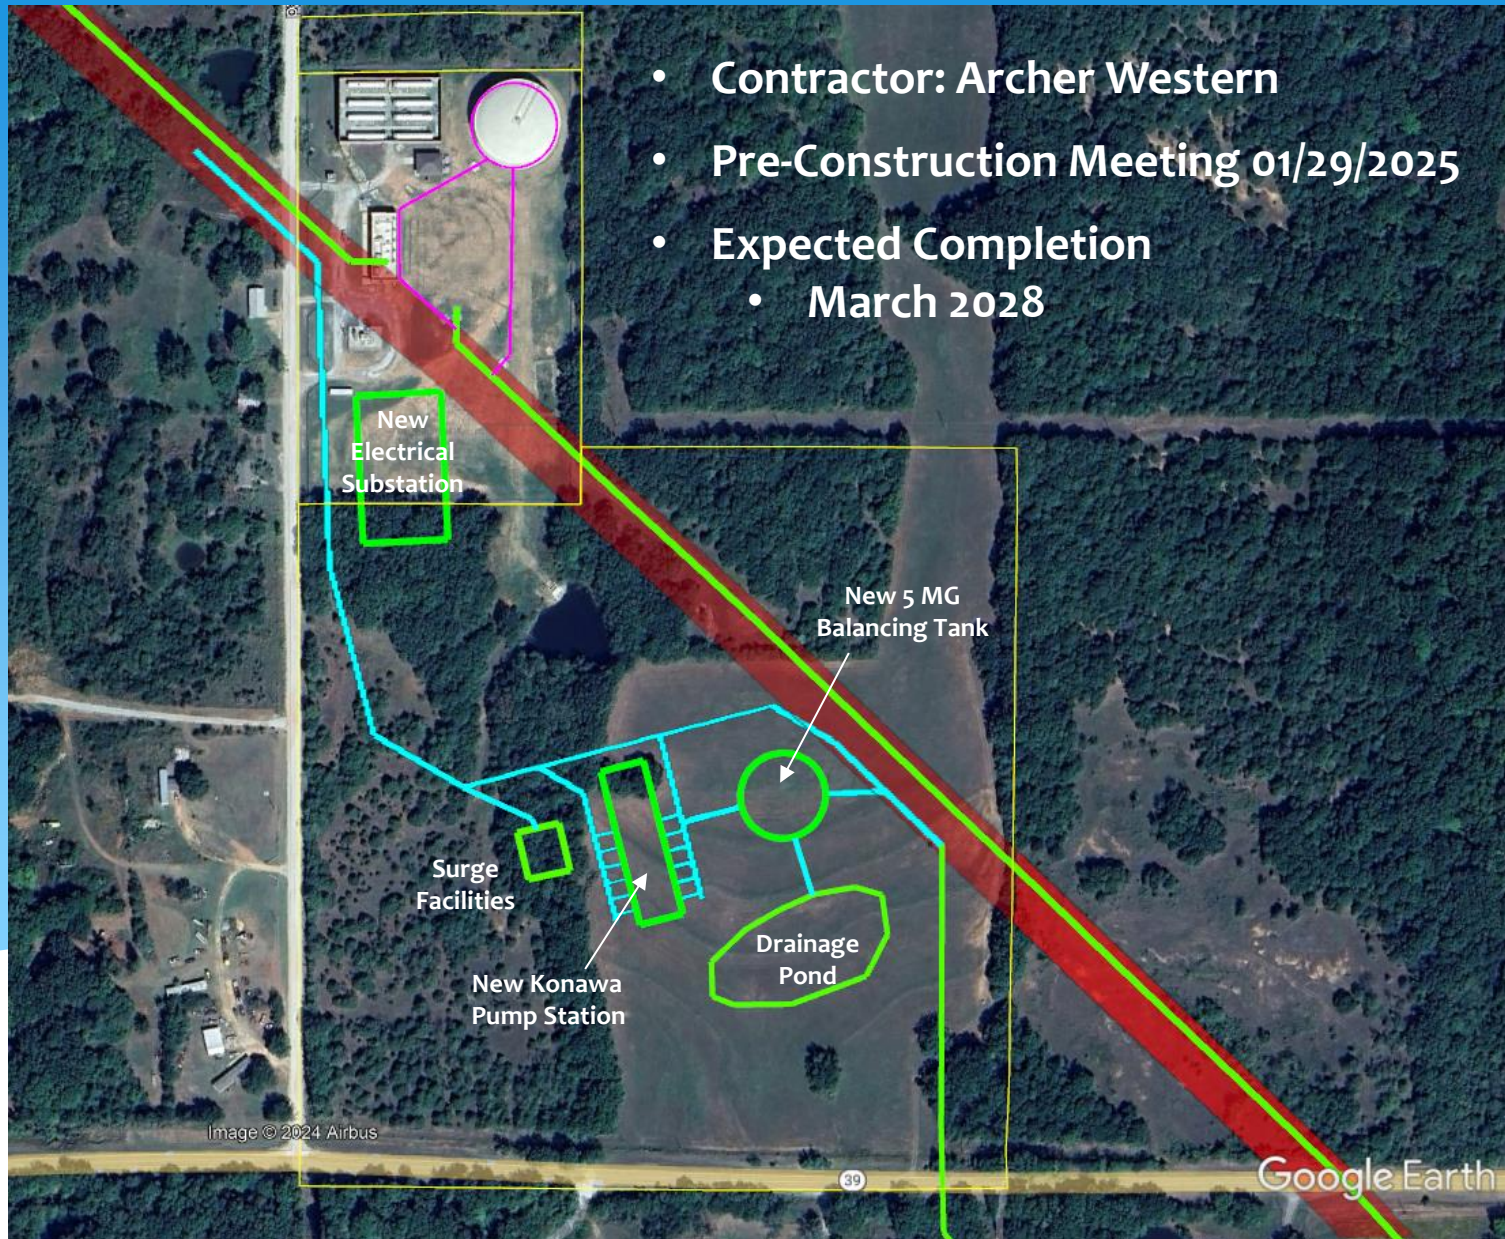




# WC-0877: Konawa to 1.44 Miles West of SH 3W





# Up Next...

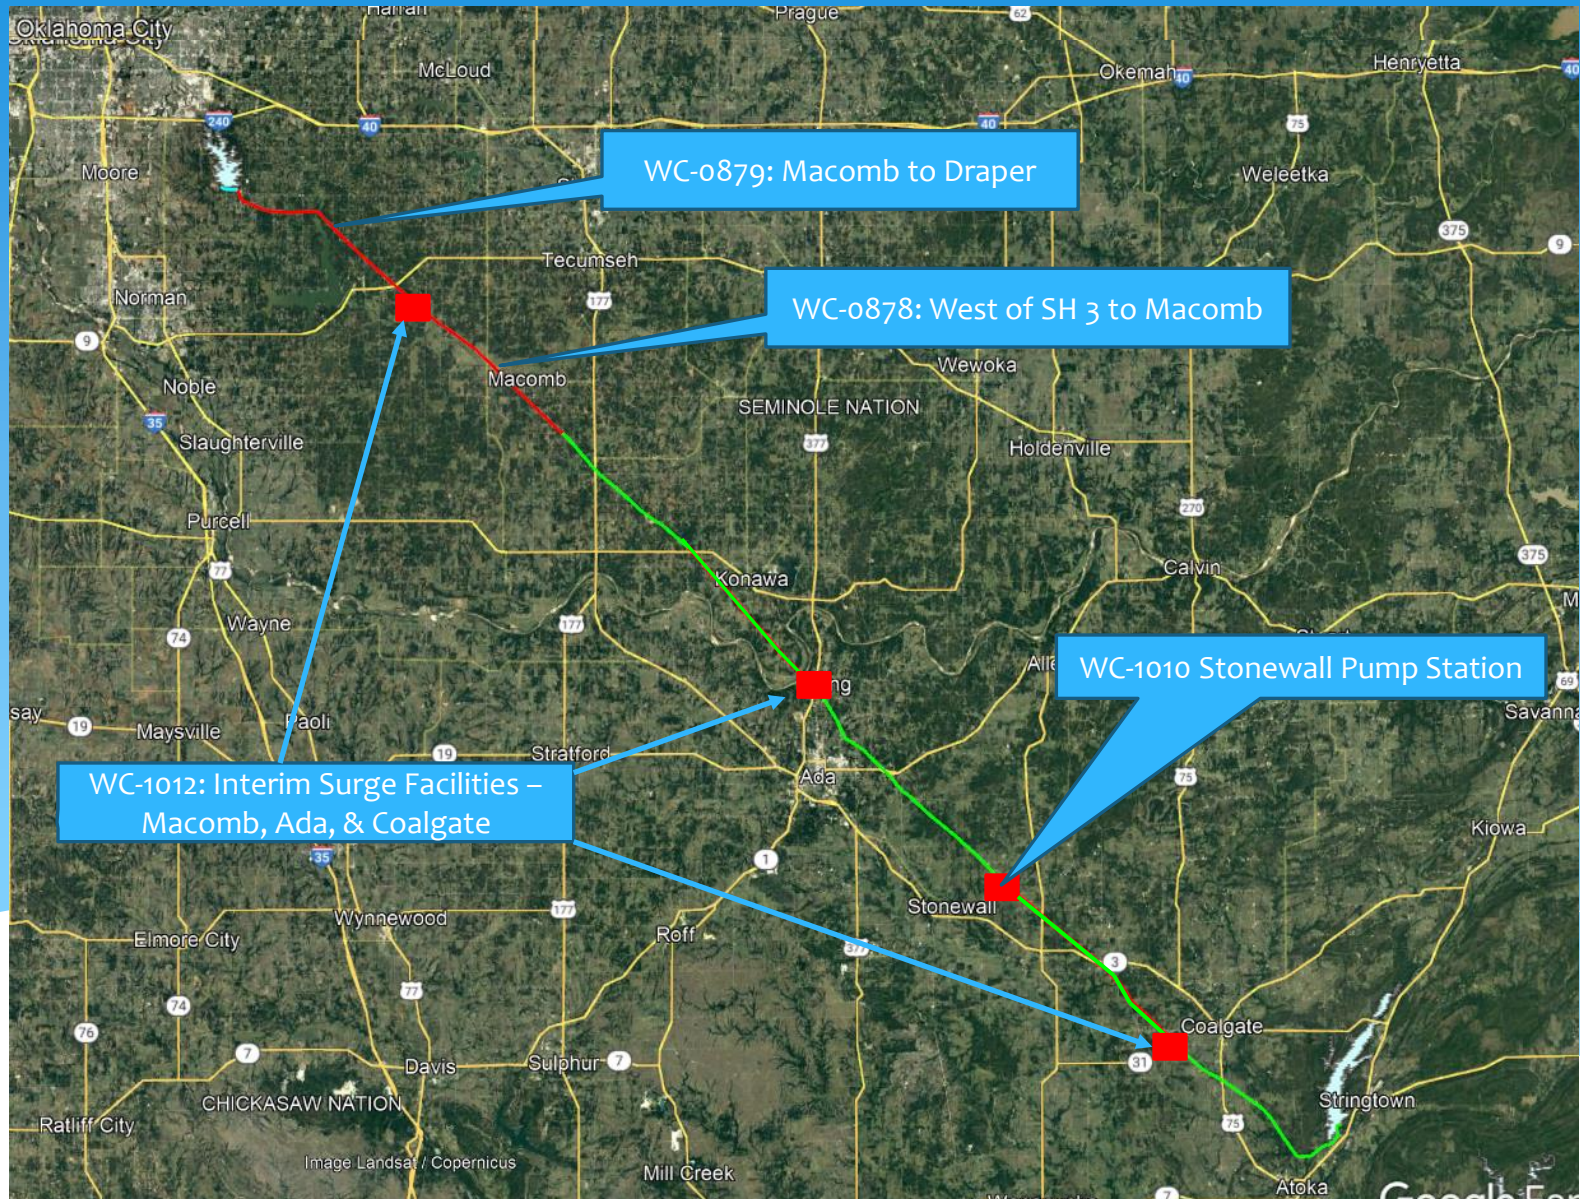



# Questions?

