


Status of Atoka Projects



Atoka Lake Road

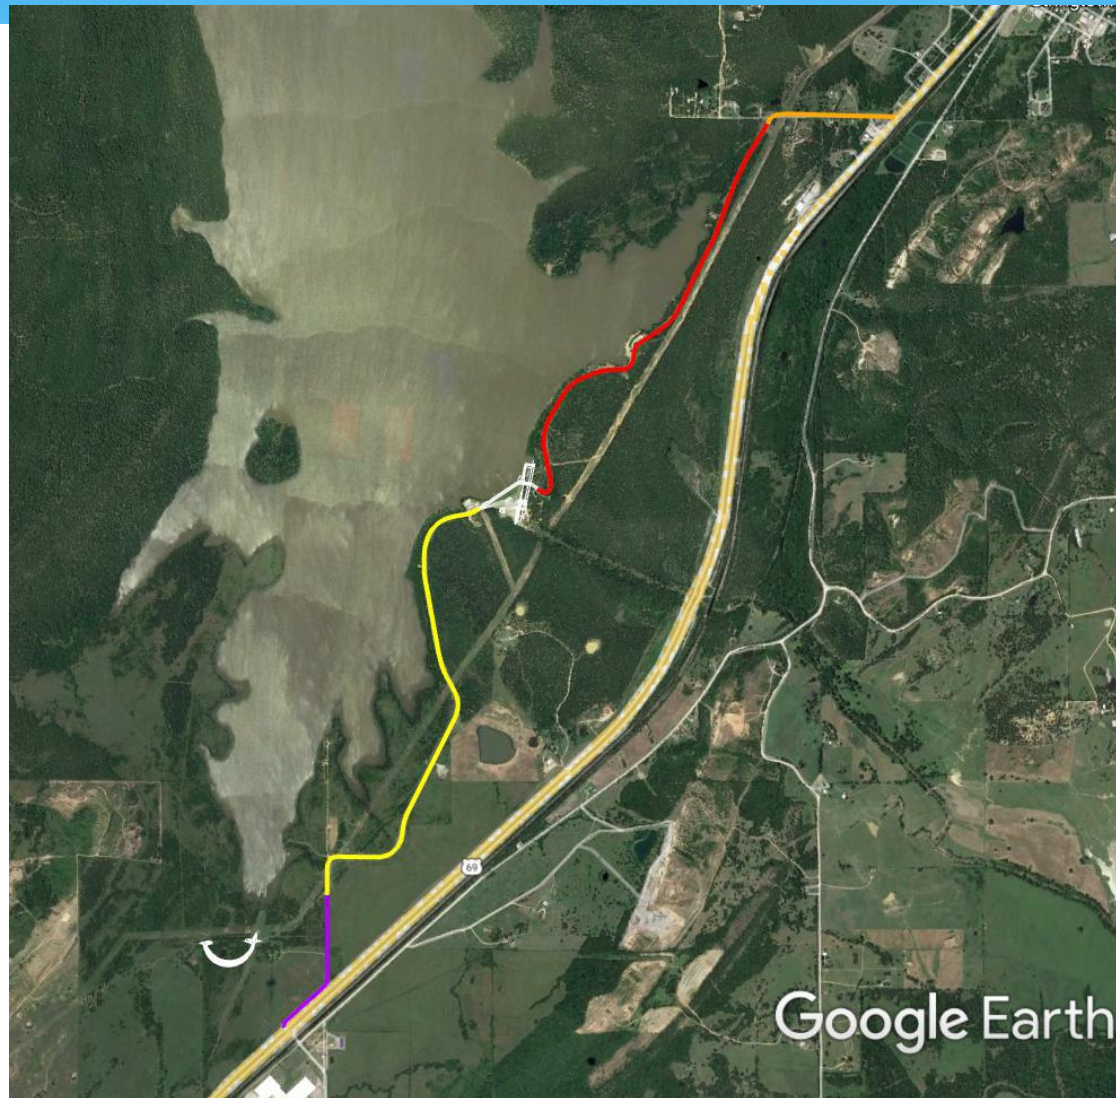

Atoka Lake Road

WM-0342

\$3.75M

Contractor:
Ellsworth Construction

Total \$7.56M


Completion End of 2024

WM-0343

\$3.70M

Google Earth

Pipeline Projects

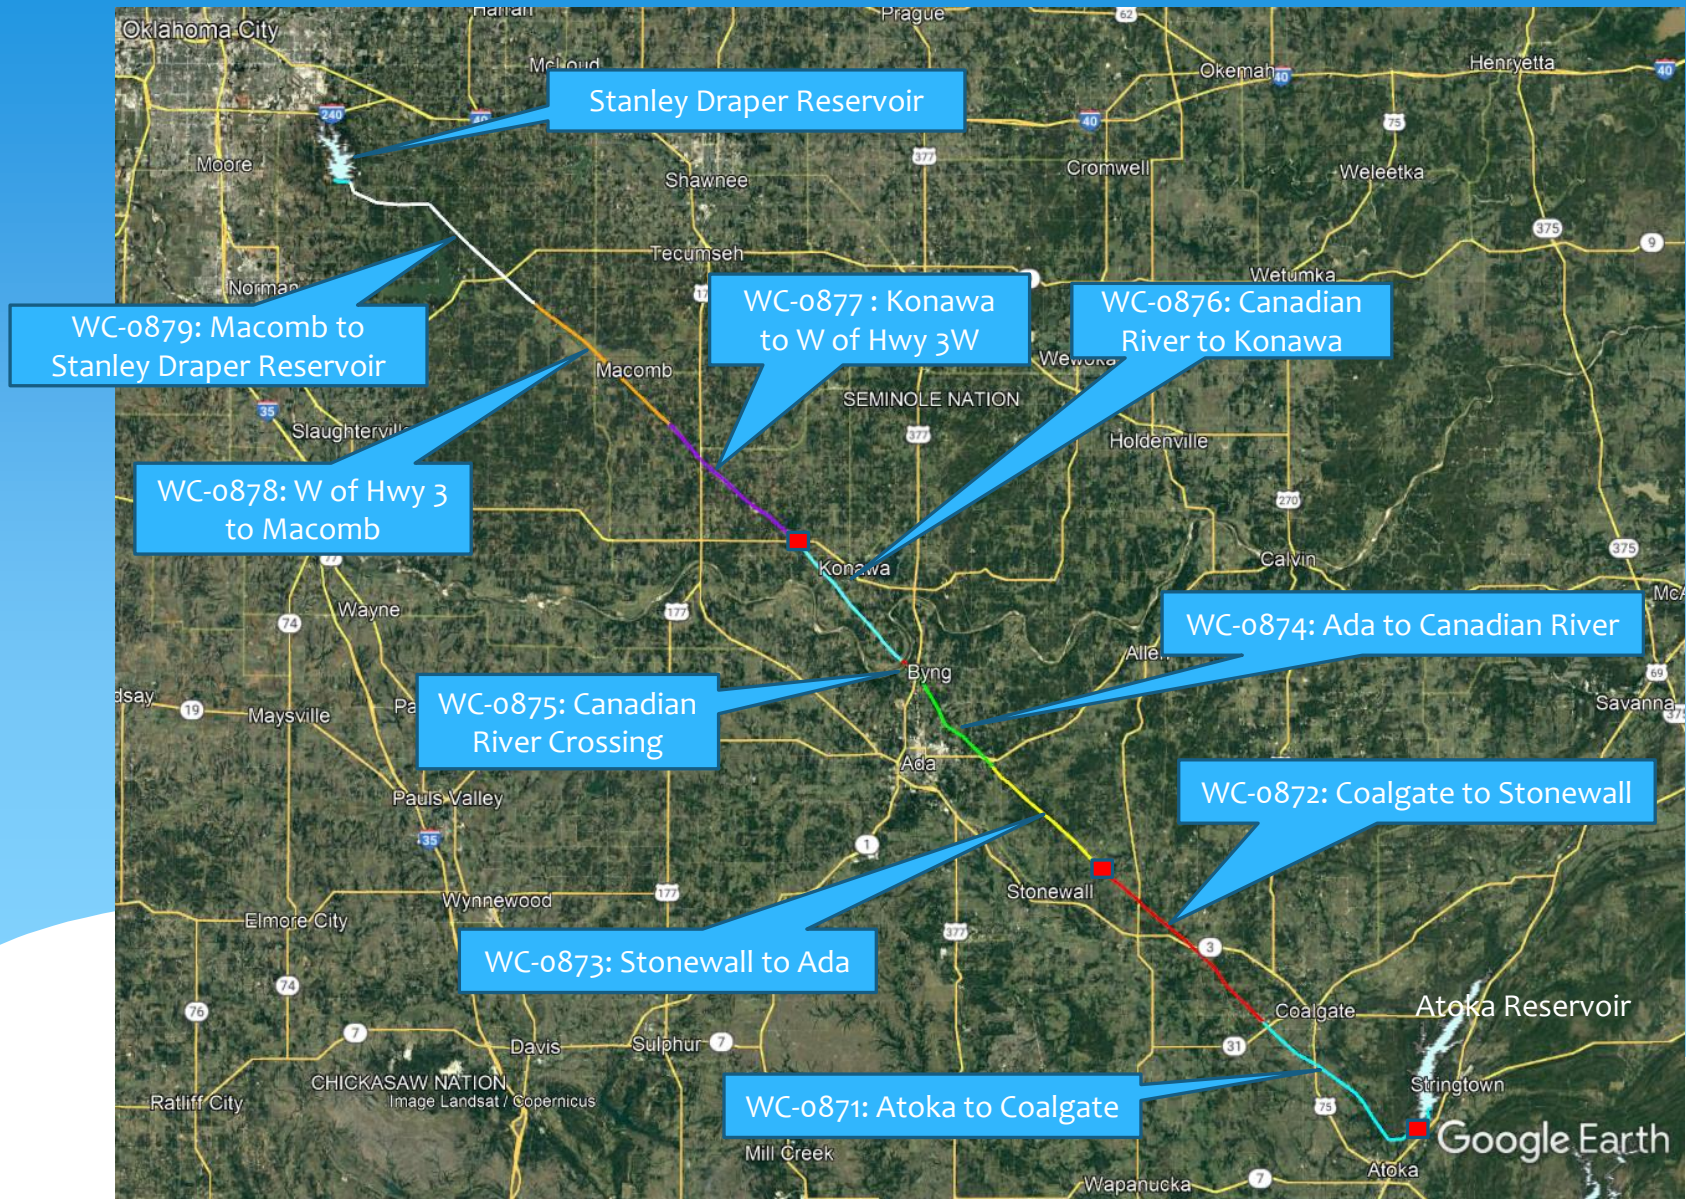

Status of Pipeline Projects

Total Length = 98.6 Miles
Under Construction = 43.0 Miles



WC-0871: Pump Station O to Coalgate

- Approx. 13.9 Miles
- Contractor
 - Oscar Renda Contracting, Inc.
- Expected Completion
 - 10/11/2025
- 56.0% Installed



Imagery Date: 3/11/2018 34°28'08.29" N 96°11'18.96" W elev. 594 ft eye alt. 16.71 mi

WC-0873: Stonewall to Ada

Ada Pump Station

- Approx. 9.6 Miles
- Contractor: McKee Utility Contractors, Inc.
- Expected Completion
 - 06/19/2025
- About 1 Mile Installed



Stonewall Pump Station

Google Earth

WC-0874: Ada to Canadian River

- Approx. 8.8 Miles
- Contractor: McKee Utility Contractors, Inc.
- Expected Completion 07/21/2024
- 98% Installed



WC-0875: Canadian River Crossing

- Contractor: Vadnais Trenchless Services, Inc.
- Expected Completion Mid-April 2024
- 99% Complete

New 60-inch

New 72-inch



© 2018 Google

Google Earth

WC-0877: Konawa to 1.44 Miles West of SH 3W



Up Next...



Questions?

